


# City Manager's Report

November 17, 2016



**CITY COUNCIL INFORMATION TRANSMITTAL  
November 16, 2016**

**The Following Council Action Requests Are Attached:**

- Follow up steps to Ms. Sherry Sells' ADA Concerns ..... 4

**Memorandums Or Items Of Information Enclosed:**

- Quarterly Progress Updates on Capital Projects ..... 5
- Upcoming Public meetings & Events ..... 15
- Scheduled City Council Agenda Items/Policy Issues ..... 18
- Status of Choke Canyon/Lake Corpus Christi Reservoir System ..... 21

**CITY COUNCIL ACTION REQUESTS (CCARS)  
As of November 16, 2016**

<b>Ref. No.</b>	<b>Date Requested</b>	<b>Action Request</b>	<b>Staff Assigned</b>	<b>Current Status</b>	<b>Est. Completion Date</b>
1.	Vaughn 11/15/16	Provide a memo to Council addressing the request for rezoning notices placed at the property to be rezoned be printed on larger placards.	Mark Van Vleck	Working	12/7/16
2.	McIntyre 11/15/16	Provide a memo to Council that provides recommended zoning for transitional housing facilities for implementation into the Unified Development Code.	Mark Van Vleck	Working	1/25/17
3.	CM 11/15/16	Provide a memo to Council that discusses the follow up steps taken regarding the concerns of Mr. Richard Wills who voiced permit concerns related to repairing his home at the Council meeting on 11/15/16.	Mark Van Vleck	Working	11/23/16
4.	CM 11/15/16	Provide a memo to Council that discusses the follow up steps staff has taken regarding the concerns of Ms. Sherry Sells who voiced ADA concerns at the 11/15/16 Council Meeting.	Miles Risley	Enclosed	11/17/16
5.	Vaughn McIntyre 10/25/16	Provide a memo to Council that includes the Interlocal Agreement with the County regarding the Health District.	Annette Rodriguez	Working	11/23/16
6.	CM 10/18/16	Provide a memo to Council that discusses the status of the JLUS implementation.	Mark Van Vleck	Working	12/13/16
7.	McIntyre 9/27/16	Provide a memo for Council that updates Council Members on Cleaning outflows, Include the Gollihar outflow.	Mark Van Vleck	Working	12/7/16
8.	Magill 9/27/16 9/20/16	Schedule a Workshop with Council Members to understand Alternative Financing Options.	Constance Sanchez	Working	1/12/17
9.	McIntyre 9/20/16	Provide a memo to Council that discusses a Process for evaluating requests for access to HOT funds.	Jay Ellington	Working	12/7/16
10.	Vaughn 9/20/16	Provide a memo to Council that will discuss succession planning for retiring employees and a waiting period for hiring as consultants.	Steve Viera	Working	12/7/16
11.	Magill 9/13/16	Present to Council the Data related to the Red Light Camera Contract before the 30-day window for renewal. (January or March)	Chief Markle	Working	1/12/17
12.	Scott 8/9/16	Provide a memo to Council that demonstrates how staff will recommend the expenditure of funds from the different resources for a Residential Street Reconstruction Program.	Mark Van Vleck	Working	11/30/16
13.	Scott 7/26/16	Provide a memo to Council that demonstrates a ten-year plan for Streets. Include Residential Street Reconstruction.	Mark Van Vleck	Working	11/30/16
14.	Mayor 5/10/16	Bring forward to Council an Affordable Housing plan before the next Tax Foreclosure Sale is presented to Council.	Jay Ellington	Working	1/24/17



# INFORMAL STAFF REPORT

## MEMORANDUM

**To:** Margie Rose, City Manager *MR*  
**From:** Miles Risley, City Attorney *MR*  
**Date:** November 18, 2016  
**Subject:** Follow-up Steps to Ms. Sherry Sells' ADA Concerns at 11/15/16 Council Meeting

**Issue/Problem:** Ms. Sells expressed concerns at the 11/15/16 Council Meeting related to the Americans with Disabilities Act (ADA).

**Background & Findings:** Several persons have indicated concern to City Council on repeated occasions regarding ADA-related enforcement or City ordinances or state law related to the ADA. The City has answered the same questions multiple times with each complainant. These citizens include Jack Gordy and Sherry Sells and her husband.


**Conclusion:** To reduce the incidence of inefficient, duplicated, inconsistent, or redundant responses, Sylvia Wilson, the City's Human Relations administrator, on behalf of the Legal Department, will establish and maintain a log of questions, requests, and answers to each of the aforementioned frequent citizen communicators. This log will be available to provide reference for answers to City Council.

With respect to Mr. and Mrs. Sells, they have had frequent and ongoing contact with City staff in Development Services, the Police Department, the Legal Department, and Human Relations. To begin addressing their issues in a more comprehensive manner, Sylvia Wilson conferenced with Mr. Sells today. She is making a comprehensive list of Mr. and Mrs. Sells' concerns and City responses.

One of Mr. Sells' complaints is that the City issues certificates of occupancy (CO's) without first obtaining inspections by registered accessibility specialists. Mr. Sells' latest request is for City building inspectors to reinspect all construction performed since March 15, 2012 (the effective date of Texas' latest building accessibility standards - <https://www.license.state.tx.us/ab/2012TAS/2012tascomplete.pdf>). The City is not required to conduct such reinspections, but we will coordinate with Development Services and provide a full answer to her question concerning the City's regulatory obligations.

On September 13th, Mr. Sells gave a list of 96 addresses of businesses with alleged ADA violations to Ms. Wilson. He requested the City inspect these businesses for ADA compliance. City Human Relations procedures require grievances to proceed with review of alleged violations. Consequently, Ms. Wilson asked Mr. Sells to complete a grievance form for each business with alleged ADA violations. To this date, Mr. Sells has not provided Ms. Wilson with grievance forms alleging ADA violations by his listed businesses.

If you have any questions or concerns, please contact me at [milesr@cctexas.com](mailto:milesr@cctexas.com) or phone 826-3873.



# INFORMAL STAFF REPORT

## MEMORANDUM

---

**To:** Margie C. Rose, City Manager *MR*

**Thru:** Mark Van Vleck, Assistant City Manager *MV*  
Valerie H. Gray, P.E., Executive Director of Public Works *VHG*

**From:** Jeffrey Edmonds, P.E., Director of Capital Programs *JE*

**Date:** November 11, 2016

**Subject:** Quarterly Progress Update on Capital Projects

---

**ISSUE:**

In September, 2015, City Council requested a quarterly update on capital projects.

**BACKGROUND:**

Engineering Services has prepared the attached Gantt charts reflecting statuses for the 2012 Bond, 2014 Bond and current CIP Projects.

**CONCLUSION:**

The 3rd Quarter 2016 "Quarterly Status Report on Capital Projects" is attached.

# BOND 2012 PROPOSITION 1

(AS OF 31 OCTOBER 2016)

PROJECT TITLE	STATUS	BUDGET \$(000s)		AE	Constr. Start Date	2015					2016					2017					2018					2019					2020																																								
		STREET	UTILITY			J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
Horne Rd (Ayers St to Port Avenue)	Complete	\$2,264	\$1,418	NEI	Aug-15	█																																																																	
JFK Causeway Area Imps	Complete	\$676	\$0	Urban	Jan-16	█																																																																	
McArdle Rd (Whitaker Dr to Ennis Joslin Rd)	Constr.	\$2,678	\$7,594	LJA	May-14	█					41 Months					X																																																							
					May-14	█					38 Months					X					Contract enforcement initiated by staff																																																		
S Staples St (Morgan Ave to IH 37)	Constr.	\$7,671	\$7,878	NEI	Sep-15	█					24 Months																																																												
					Sep-15	█					24 Months										No change since last quarter																																																		
Navigation Blvd (Up River Rd to Leopard St)	Constr.	\$6,627	\$7,209	LNV	Apr-16	█					15 Months																																																												
					Apr-16	█					15 Months										No change since last quarter																																																		
Williams Dr (Staples St to Airline Rd) (TXDOT)	Constr.	\$4,697	\$5,202	LJA	May-16	█					15 Months																																																												
					Feb-16	█					16 Months					X					AT&T duct bank conflict, Corrected construction schedule																																																		
Ocean Dr (Buford St to Louisiana Ave)	Constr.	\$9,112	\$8,550	FNI	Jun-16	█					18 Months																																																												
					Jun-16	█					18 Months										No change since last quarter																																																		
Kostoryz Rd (Brawner Pkwy to Staples St)	Constr.	\$5,856	\$4,181	Urban	Aug-16	█					17 Months																																																												
					Aug-16	█					17 Months										No change since last quarter																																																		
Greenwood Dr (Gollihar Rd to Horne Rd)	Constr.	\$2,096	\$1,994	Govind	Sep-16	█					11 Months																																																												
					Sep-16	█					11 Months										No change since last quarter																																																		
Tuloso Rd (IH37 to Leopard St)	Bid	\$1,910	\$3,050	MEI	Dec-16	█					8 Months																																																												
					Jan-17	█					8 Months										AE unable to meet schedule																																																		
S Alameda St (Ayers St to Louisiana Ave)	Redesign	\$2,988	\$3,482	HDR	Jan-17	█					15 Months																																																												
					Mar-17	█					15 Months										AE unable to meet schedule																																																		
Holly Road (Crosstown to Greenwood Dr) (TXDOT)	Redesign	\$6,557	\$5,182	LNV	Jan-17	█					18 Months																																																												
					May-17	█					18 Months										18 Months					On hold due to Environmental Clearance																																													
S Staples St (Brawner Pkwy to Kostoryz Rd)	Redesign	\$6,592	\$4,865	FNI	Apr-17	█					18 Months																																																												
					Sep-17	█					18 Months										18 Months					Redesign for MPO bike plan																																													
Morgan Ave (Staples St to Crosstown Freeway)	On Hold	\$2,645	\$3,401	CRG	Jun-17	█					8 Months																																																												
					Apr-18	█					8 Months										8 Months					On hold pending hospital construction																																													
Yorktown Blvd (Rodd Field to Cimarron) (Landscape) (Street and Utility improvements completed Aug 2014)	Pending	\$300	\$3,185	FNI	-	█																																																																	
Leopard St (Crosstown to Palm Dr)	Deferred	\$2,050	\$1,942	HDR	-						Deferred					No change since last quarter																																																							
					-						Deferred					No change since last quarter																																																							
Twigg St (Shoreline Blvd to Lower Broadway)	Deferred	\$1,250	\$2,551	HDR	-						Deferred					No change since last quarter																																																							
					-						Deferred					No change since last quarter																																																							
ADA Master Plan Improvements	Ongoing	\$2,300	\$0	CH2M	-						Ongoing										Ongoing																																																		
					-						Ongoing										Ongoing																																																		
Signal Improvements & Street Lighting	Ongoing	\$1,188	\$0	MBITS	-						Ongoing										Ongoing																																																		
					-						Ongoing										Ongoing																																																		
TxDOT Participation	Ongoing	\$1,064	\$2,670	LNV	-						Ongoing										Ongoing																																																		
					-						Ongoing										Ongoing																																																		






# BOND 2014 PROPOSITION 1

(AS OF 31 OCTOBER 2016)

PROJECT TITLE	STATUS	BUDGET \$(000s)		AE	Constr. Start Date	2015					2016					2017					2018					2019					2020																																								
		STREET	UTILITY			J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
Waldron Rd (Airdome Dr to Caribbean Dr)	Complete	\$2,031	\$1,625	Urban	Aug-15	[Construction Complete]																																																																	
Santa Fe St (Elizabeth St to Hancock St)	Complete	\$1,700	\$149	MEI	Mar-16	[Construction Complete]																																																																	
Southern Minerals Rd (Up River Rd to IH-37)	Pending	\$2,445	\$1,015	LNV	Sep-16	[On Hold / Pending]																																																																	
					Jan-17	[On Hold / Pending] 10 Months Additional delays for private gas pipeline & AEP poles adjustments																																																																	
Alameda St (Kinney St to Lipan St)	Bid	\$1,500	\$704	LAN	Dec-16	[On Hold / Pending] 6 Months																																																																	
					Dec-16	[On Hold / Pending] 6 Months No change since last quarter																																																																	
Ayers St (Alameda St to Ocean Dr)	Redesign	\$3,900	\$4,323	FNI	Dec-16	[Redesign] 12 Months																																																																	
					Mar-17	[Redesign] 12 Months Design phase extended to capture savings for utilities																																																																	
Gollihar Rd (South Staples to Weber Rd)	Redesign	\$7,499	\$8,200	NEI	Jan-17	[Redesign] 27 Months																																																																	
					Apr-17	[Redesign] 24 Months Design revised to incorporate MPO plan and coordinate construction phasing																																																																	
Gollihar Rd (Weber Rd. to Carroll Ln.)	Redesign	\$3,700	\$3,945	LJA	Jan-17	[Redesign] 16 Months																																																																	
					Apr-17	[Redesign] 12 Months Design revised to incorporate MPO plan and coordinate construction phasing																																																																	
Gollihar Rd (Carroll Ln to Kostoryz Rd)	Redesign	\$3,700	\$4,900	LJA	Jan-17	[Redesign] 16 Months																																																																	
					Apr-18	[Redesign] 12 Months Revised to correctly indicate sequential construction instead of concurrent																																																																	
Yorktown Blvd (Everhart Rd to Staples St)	Redesign	\$7,663	\$3,057	FNI	Dec-16	[Redesign] 15 Months																																																																	
					May-17	[Redesign] 15 Months Design revised to incorporate MPO plan and coordinate construction phasing																																																																	
Corona Dr (Flynn Pkwy to Everhart Rd)	Redesign	\$3,200	\$1,256	Govind	Jan-17	[Redesign] 12 Months																																																																	
					May-17	[Redesign] 9 Months Delayed due to land acquisition and AE unable to meet schedule																																																																	
Carroll Lane (Houston St to McArdle Rd)	Redesign	\$3,206	\$2,284	MGM	Feb-17	[Redesign] 12 Months																																																																	
					Jun-17	[Redesign] 12 Months Design revised to incorporate MPO plan and coordinate construction phasing																																																																	
Staples St (Alameda St to Morgan St)	Redesign	\$2,900	\$1,100	HDR	Jan-17	[Redesign] 14 Months																																																																	
					Jul-17	[Redesign] 14 Months AE unable to meet schedule																																																																	
Yorktown Blvd (Lake Travis to Everhart Rd)	Redesign	\$4,197	\$1,025	LNV	Feb-17	[Redesign] 14 Months																																																																	
					Aug-17	[Redesign] 14 Months Design revised to incorporate MPO plan and coordinate construction phasing																																																																	
Old Robstown Rd (Highway 44 to Leopard St)	Redesign	\$4,367	\$612	CH2M	Feb-17	[Redesign] 15 Months																																																																	
					Sep-17	[Redesign] 12 Months Design extended for additional coordination with RTA, coordinate construction phasing																																																																	
Morgan Ave (Staples St to Ocean Dr)	On Hold	\$2,800	\$2,889	CRG	Jun-17	[On Hold / Pending] 14 Months																																																																	
					Dec-18	[On Hold / Pending] 14 Months On hold pending Hospital construction																																																																	
ADA Master Plan Improvements - Citywide	SPMP	\$2,300	\$181	-	-	[Ongoing]																																																																	
					-	[Ongoing] Combined with Bond 2012 project																																																																	


















# INFORMAL STAFF REPORT

## MEMORANDUM

---

**To: Mayor and Council**

**From: Margie C. Rose, City Manager**

**Date: November 17, 2016**

**Subject: Upcoming Public Meetings and Events**

---

For your convenience, attached is a calendar of upcoming public meetings and events, as submitted by City departments.

Please keep in mind that the City's Ethics Ordinance prohibits Council members from speaking before City boards, commissions, and committees, except on behalf of your own personal financial interest, in which case you are to immediately state so publicly to the board, commission or committee.

We hope this calendar will keep you informed about activities of interest taking place in your district and Citywide.

If you have any questions, please feel free to contact me.

**November 22, 2016**

Tuesday

11:30 AM - 5:00 PM

NO COUNCIL MEETING -- NO COUNCIL MEETING

**November 23, 2016**

Wednesday

1:30 PM - 2:30 PM

Board of Adjustment -- City Hall, Council Chambers

**November 28, 2016**

Monday

All Day

Transportation Advisory Committee -- City Council Chambers

**November 29, 2016**

Tuesday

11:30 AM - 5:00 PM

NO COUNCIL MEETING -- NO COUNCIL MEETING

**December 1, 2016**

Thursday

5:00 PM - 6:00 PM

Human Relations Commission -- City Council Chambers

**December 6, 2016**

Tuesday

10:30 AM - 11:30 AM

Library Board Room -- La Retama Central Library - 2nd Floor Board Room

11:30 AM - 5:30 PM

NO COUNCIL MEETING -- NO COUNCIL MEETING

4:00 PM - 5:00 PM

Arts & Cultural Commission (ACC) Regular Meeting -- City Hall, 6th floor

**December 7, 2016**

Wednesday

3:00 PM - 5:00 PM

Committee for persons with Disabilities -- Council Chambers

**December 13, 2016**

Tuesday

11:30 AM - 5:30 PM

COUNCIL MEETING -- Council Chambers

**December 14, 2016**

Wednesday

5:00 PM - 6:00 PM

Parks and Recreation Advisory Committee -- City Hall, 3rd floor Conference Room

**December 20, 2016**

Tuesday

11:30 AM - 5:30 PM

COUNCIL MEETING -- Council Chambers

**December 21, 2016**

Wednesday

5:30 PM - 6:30 PM

Community Youth Development Program Steering Committee -- Juvenile Assessment Center, 615 Leopard Suite 105

**CITY OF CORPUS CHRISTI  
SCHEDULED  
CITY COUNCIL AGENDA ITEMS/POLICY ISSUES  
As of November 18, 2016**

**\*Please note that this schedule may change at anytime due to scheduling  
conflicts and/or priority issues.**

- (T) – Indicates Tentative Scheduling

**December 13, 2016**

**\*Regular Meeting 11:30 a.m.**

1. (16-0888) Approving a resolution to renew a Small Business Incentives Agreement between the Corpus Christi Business and Job Development Corporation and Del Mar College (Del Mar) to provide a grant up to \$48,490 for their Procurement Technical Assistance Center (PTAC) to assist small business.
2. (16-1102) Approving a resolution to renew a Small Business Incentives Agreement between the Corpus Christi Business and Job Development Corporation and Texas A&M University - Corpus Christi (TAMU-CC) to provide grant up to \$150,000 for their internship program to assist small businesses
3. (16-1103) Approving a resolution to renew a Small Business Incentives Agreement between the Corpus Christi Business and Job Development Corporation and Del Mar College (Del Mar) to provide grant up to \$150,000 for their internship program to assist small businesses.
4. (16-1212) Closing a utility easement out of a part of Lot 16, Block 8 of Hopper Addition No. 2 located at 3749 Pope Drive. Ordinance abandoning and vacating a 0.028-Acre portion of an existing utility easement out of a part of Lot 16, Block 8 of Hopper Addition No. 2, located at 3749 Pope Drive and requiring the owner, Fernando Fernandez, to comply with the specified conditions.
5. (16-1233) Motion authorizing the City Manager or his designee to renew a lease agreement with One Shoreline Plaza, LLC, for ten years with an optional extended term of ten years and approving monthly lease payments of \$13,040 per month with annual rent increase of 3%, for rooftop space and equipment room necessary to support the public safety communications system.
6. (16-1265) Resolution finding the lowest responsive, responsible bidder for round maintenance services by group in response to Bid Nos. 138, 139, 140, 141, 142, 143, 144, 145, and 146; awarding a one-year service agreement, with two one-year renewals, to the lowest responsible bidder per bid number; and authorizing the City Manager or designee to execute the service agreements.

Cut masters Lawn Service  
Corpus Christ, Texas  
Group 1, 11, 12, 13, 14, 16  
\$167,349.66

Dorame General Repair  
Corpus Christi, Texas  
Group 9, 10, 15  
\$66,172.04

Grand Total \$233,521.70

7. (16-1269) Ordinance closing, vacating, and abandoning a previously developed and surfaced 67,693-square foot (1.55 acres) portion of a public right-of-way, as shown on the recorded plat of Manhattan Estates Unit 6, a map of which is recorded in Volume 68, Pages 392 and 393, Map Records of Nueces County, Texas, and requiring the abutting owners to comply with specified conditions; and providing an effective date.
8. (16-1300) Motion authorizing the City Manager or the City Manager's designee to execute a radio facility and tower lease agreement with KVOA Communications, Inc. d.b.a. KRIS Communications for a 5 year term estimated at \$36,414 per year from January 1, 2016 through December 31, 2020 and for an optional extended term of 5 years estimated at \$36,414 per year from January 1, 2021 through December 31, 2025, for continued use as a communications site to operate a public safety communications system.
9. (16-1303) Motion authorizing the City Manager or designee to execute a five-year service agreement with Gray CPA Consulting, PC, of Magnolia, Texas, for the purchase and implementation of Comprehensive Annual Financial Report (CAFR) and Budget Book software licenses for a total amount of up to \$337,310 and providing for a contingency amount of up to \$10,000 each for the Finance Department and Budget Office related to this software procurement.
10. (16-1312) Resolution reaffirming the City of Corpus Christi's Investment Policy and Investment Strategies for Fiscal Year 2016-2017
11. (16-1318) Closing a utility easement out of a part of Lot 16, Block 8 of Hopper Addition No. 2 located at 3749 Pope Drive. Ordinance abandoning and vacating a 0.028-Acre portion of an existing utility easement out of a part of Lot 16, Block 8 of Hopper Addition No. 2, located at 3749 Pope Drive and requiring the owner, Fernando Fernandez, to comply with the specified conditions.
12. (16-1349) Ordinance amending Fiscal 2017 operating budget to move funds for Street Preventative Maintenance Program (SPMP) from Fund 1041 (Streets Fund) to Fund 1043 (SPMP Fund).
13. (16-1356) Ordinance authorizing the City Manager or designee to execute a lease agreement with Driscoll Children's Hospital for hangar, office and parking space at the Corpus Christi International Airport for a lease term of three years, with an option to renew for two additional one-year periods.

- 14.(16-1358) Ordinance amending the Code of Ordinances, City of Corpus Christi, Chapter 55, Utilities, Subsection (a)(2)e regarding Resale Treated Water Rates; providing for publication and effective date of January 1, 2017.
- 15.(16-1362) Resolution authorizing the City Manager or designee to enter into an outside city limits water contract with John C. Avila to provide public water to their property located outside the city limits described as Robertson William J. Farm Tracts, 1 Acre out of Lot 5-A Tract 20; also commonly known by its street address as 6917 Jurica Road under Section 55-111, Code of Ordinances.
- 16.(16-1363) Ordinance authorizing city manager or designee to execute a water arterial transmission and grid main construction and reimbursement agreement (“Agreement”) with MPM Development, L.P. (“Developer”), for the Construction of a water arterial transmission and grid main line and appropriating \$7,324.00 from the No. 4030 Arterial Transmission and Grid Main Trust Fund to reimburse the Developer in accordance with the Agreement.
- 17.(16-1364) Approving the Corpus Christi Business and Job Development Corporation’s amended Guidelines and Criteria for granting Business Incentives
- 18.(16-1366) Resolution authorizing the City Manager or designee to execute an Interlocal Cooperation Agreement with the Department of State Health Services (DSHS), in an amount not to exceed \$56,000.00, to provide laboratory services for the analysis of bay water samples for the contract period of September 1, 2016, through August 31, 2018; and to ratify acceptance of the agreement to begin as of September 1, 2016.
- 19.(16-1368) Ordinance authorizing the City Manager or designee to execute all documents necessary to accept, amend, and appropriate a grant contract for the Women, Infant and Children’s Nutrition Program (WIC) grant in the amount of \$1,012,631.00, from the Texas Department of State Health Services in the Health Grants Fund No. 1066, to provide funds for the WIC program for the contract period October 1, 2016, through September 30, 2017; and ratifying acceptance of the grant agreement to begin October 1, 2016.




**December 20, 2016**

**\*Regular Meeting 11:30 a.m.**

1. (16-1241) Resolution adopting the City of Corpus Christi’s State Legislative Priorities for the 85<sup>th</sup> Texas Legislature and Federal Legislative Priorities for the 115<sup>h</sup> U.S. Congress.

STATUS OF THE CHOKE CANYON / LAKE CORPUS CHRISTI / LAKE TEXANA RESERVOIR SYSTEM

As of: 11/18/2016

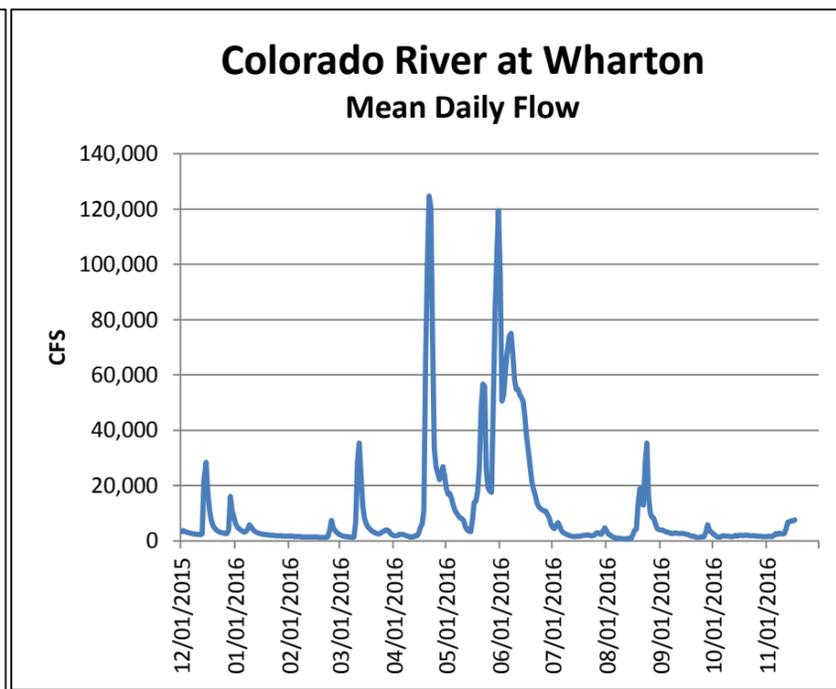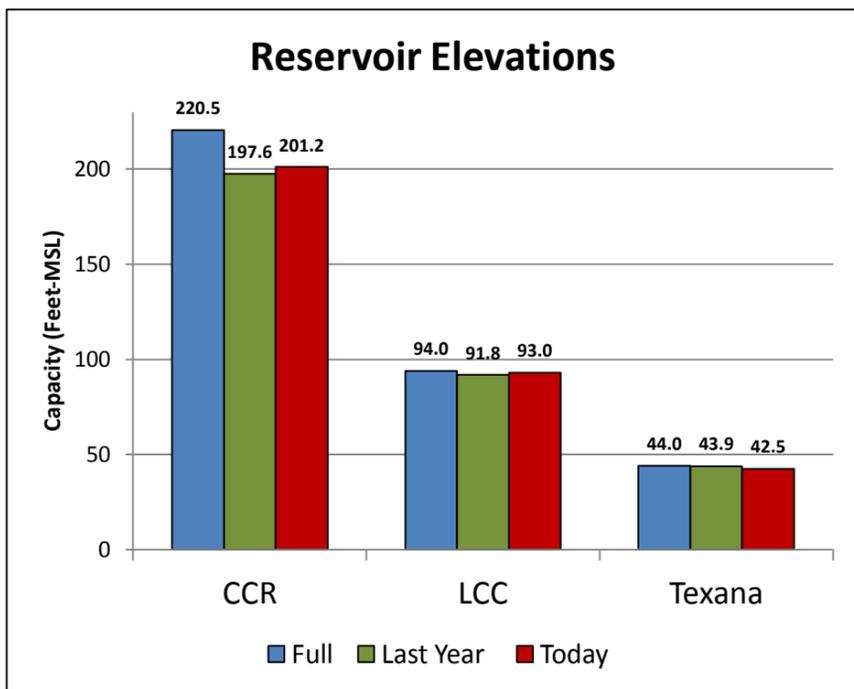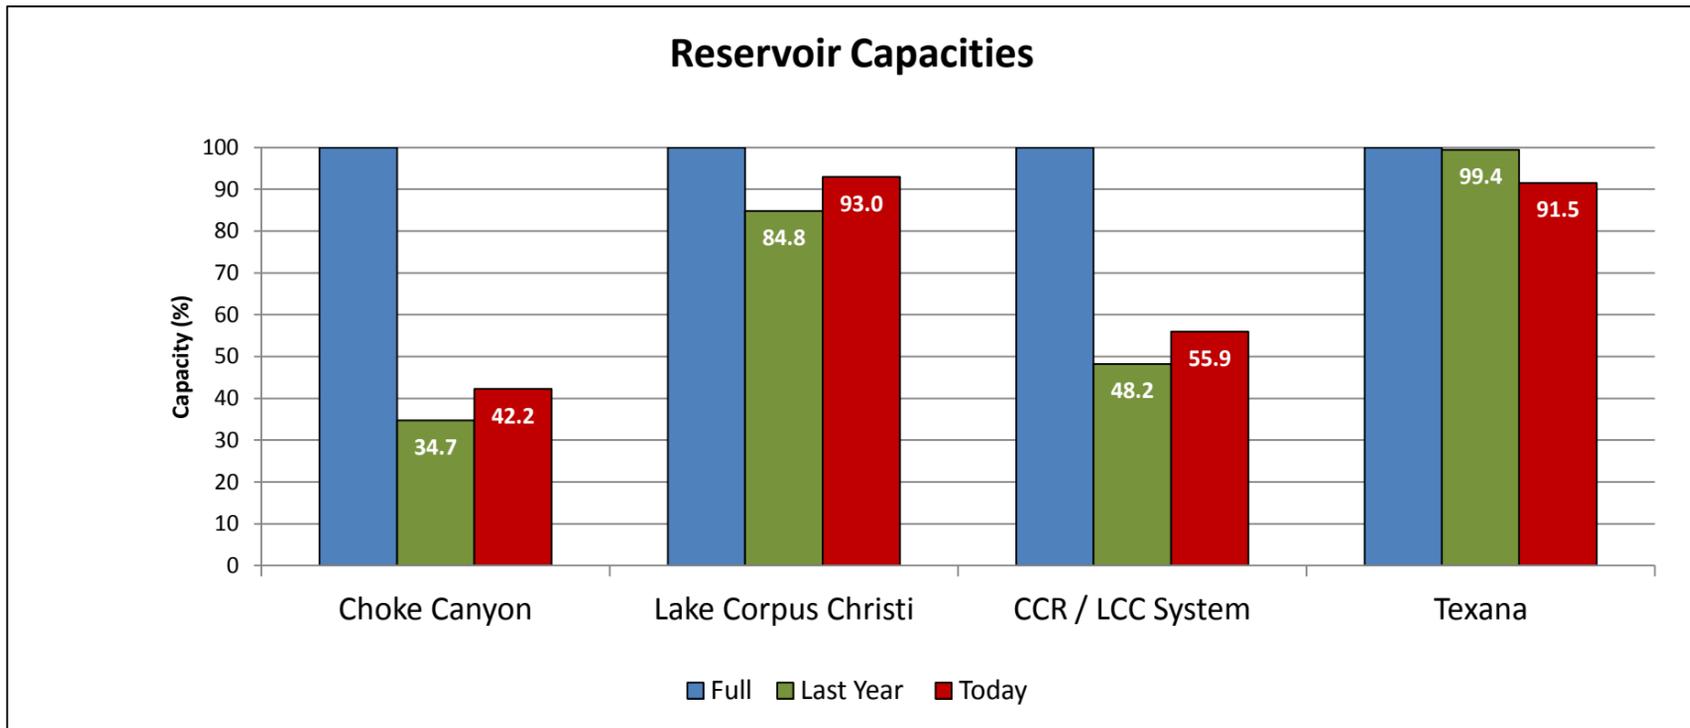

RESERVOIR STATISTICS											
Date	Choke Canyon Reservoir			Lake Corpus Christi			CCR/LCC Combined		Lake Texana		
	Elevation	Volume	% Capacity	Elevation	Volume	% Capacity	Volume	% Capacity	Elevation	Volume	% Capacity
FULL	220.5	695,271	100%	94.0	257,260	100%	952,531	100%	44.0	161,085	100%
11/18/2016	201.2	293,596	42.2%	93.0	239,193	93.0%	532,789	55.9%	42.5	147,442	91.5%
11/17/2016	201.2	294,557	42.4%	93.0	238,657	92.8%	533,214	56.0%	42.6	148,332	92.1%
10/18/2016	201.5	299,036	43.0%	92.8	235,981	91.7%	535,017	56.2%	43.2	153,730	95.4%
11/18/2015	197.6	241,185	34.7%	91.8	218,185	84.8%	459,370	48.2%	43.9	160,156	99.4%
